



Proposal Roadmap

In every challenge lies an opportunity for growth.

This document applies Kaizen's principle of embracing gaps and turning limitations into stepping stones. By seeing precisely where our processes fall short, we ignite continuous improvement and set a clear path to lasting success.

Prepared by: Daed Alqasem

Version: 03

Date: 17 December 2025



Phone

+971 56 682 8836



Email

Sales@Kaizenae.com



Address

1st Floor, Al-Masrif Building,
Sheikh
Zayed road, Dubai

Table of Contents

Cover Letter	4
Why Kaizen Principles	5
Proven Accelerators	5
Delivery Excellence	5
Fully Certified Team	5
Regional & Global	5
RFP Compliance Matrix & Feasibility Summary	6
Registration & Approval	7
Operational Model	7
Customer Support	8
Reporting & Analytics	9
Core Interfaces & Integration	9
1 Registration & Screening	11
2 Service Catalogue & Ordering	12
3 Service Fulfilment & Task Management	12
4 Vendor Collaboration & Procurement	13
6 Customer Support & Live Chat	14
7 Governance, Documents & Approvals	15
Why It Matters for KUEC	15
Data-Migration & Cleansing Plan	16
Integration Architecture	17
Training Approach: “Explain → Show → Do → Coach”	17
Training Schedule Snapshot:	19
Assumptions & Exclusions	20
SLA & Support Model	20

Project Implementation Plan & Timeline	20
On-Site Discovery First	21
Functional Delivery Tracks	21
Key Milestones & Timeline	22
Execution Principles	23
Appendix C — Proposed UI Mockups (Odoo 18 EE Theme)	23
Conclusion	33



Cover Letter

Kaizen Principles is pleased to submit our formal response to the Request for Information (RFI) issued by Khalifa University Enterprises Company (KUEC) for the development of a Partner Self-Service Catalog Portal. We regard KUEC as a beacon of innovation within the UAE's knowledge economy, and we welcome the opportunity to contribute to this forward-looking initiative.

Over the past decade, Kaizen Principles has earned a reputation for delivering comprehensive, enterprise-class solutions that harmonize robust technology with intuitive user experiences. Our multidisciplinary team combines expertise in portal design, ERP/CRM integration, and data-driven service automation—capabilities that align precisely with the functional and operational requirements outlined in your RFI.

We are committed to providing a platform that is efficient, scalable, and seamlessly integrated with the distinctive aesthetic and innovative spirit that defines KUEC. Enclosed you will find our detailed proposal, including project plans, milestone timelines, and a preliminary budget framework. These elements have been tailored to ensure the portal's successful delivery while safeguarding schedule, quality, and cost.

We believe our approach supports KUEC's mission to foster a future-oriented mindset and drive technological advancement across your stakeholder network. Thank you for considering our submission. We look forward to the possibility of collaborating with KUEC and stand ready to discuss any aspect of our proposal at your convenience.

Why Kaizen Principles

Proven Accelerators

Kaizen Principles brings 24 plug-and-play “ready-made solutions” and a library of 4,500+ pre-built developments that span every standard Odoo application. These assets shorten lead-times, cut risk, and allow us to focus project effort on the 10–20 % of functionality that is truly unique to your business.

Delivery Excellence

Metric	Credential Detail
Project success rate	100 % on-time, on-scope, go-live across all engagements.
Odoo recognition	Nominated Best Starter; Gold Partner status maintained since first accreditation—never downgraded.
Team certifications	PMP-certified project managers • Six Sigma Black Belts for process optimization • ISO-qualified implementation methodology (ISO 9001 & ISO 27001 frameworks).

Fully Certified Team

Every consultant, developer, and QA analyst on your project holds current Odoo functional and technical certifications, ensuring adherence to best practices and maintainable code.

Regional & Global

Presence Headquartered in Dubai with delivery hubs in the UAE, Saudi Arabia, Egypt, India, and Pakistan, we support clients locally while providing around-the-clock development and support coverage.

Consulting-First Approach

Before any line of code is written, our consultants map and streamline your internal processes, SLAs, and controls. Automation only follows once workflows are lean, compliant, and measured, guaranteeing that technology amplifies, rather than masks, operational excellence.

RFP Compliance Matrix & Feasibility Summary

The following Compliance Matrix provides a line-by-line assessment of KUEC's functional and technical requirements against **Odoo 18 Enterprise Edition**. For each item, we indicate one of four feasibility states:

Indicator	Meaning	Typical Effort
Standard	Fully supported by Odoo (configuration only).	Basic configuration & onboarding
Development	Achievable through customization in Odoo (Python/OWL, Studio, or bespoke modules).	Moderate development & QA
Integration	Requires interfacing Odoo with an external system or third-party service.	API work, middleware, testing
Gap / No	<i>Not available in native Odoo.</i> Substantial custom development or alternative tooling would be required.	Significant project scope

Important clarification:

Whenever the matrix shows “No,” it denotes that the requested capability does not exist in Odoo’s standard feature set. Achieving that requirement would therefore necessitate either (a) a dedicated custom module that extends Odoo far beyond typical configuration, or (b) the adoption of a specialist third-party platform.

This structured view enables KUEC to quickly gauge feasibility, budget impact, and risk for each requirement, ensuring transparent expectations before project kickoff.

Registration & Approval

Req ID	Requirement Description	Covered in Odoo?	Odoo Fit
1	Start-up Registration (portal form & docs)	No	Development
2	Start-up Registration Approval workflow	Yes	Standard
3	Start-up Sign-Up / Portal onboarding	Yes	Standard
4	Service Vendor Registration	No	Development
5	Vendor Approval by Procurement	Yes	Standard
6	Vendor Account Activation & Dashboard	No	Development
7	Automatic Notifications on registration	Yes	Standard
8	Cancel / Disqualify Start-up (≤ 1 yr)	No	Development
9	Cancel Approved Vendor & final billing	No	Development

Operational Model

Req ID	Requirement Description	Covered in Odoo?	Odoo Fit
10	Customer profile & segmentation	No	Development
11	Vendor classification & star rating	No	Development
12	Service/package pricing with discounts	No	Development
13	Smart service-to-vendor routing	No	Development

14	Onboarding package (22 services)	No	Development
15	Service catalogue browsing	Yes	Standard
16	Business-matrix eligibility rules	No	Development
17	Purchase package/request quotation	Yes	Standard
18	CRM update after purchase	Yes	Standard
19	Auto / manual service assignment	No	Development
20	Fulfilment journeys (project & retainer)	No	Development
21	SR communication thread & docs	Yes	Standard
22	Customer satisfaction survey	Yes	Standard
23	Iterative service-card deployment	No	Development
24	Service cancellation & refund flow	No	Integration
25	Wallet/card refund (on-time payers)	No	Integration
26	Invoice cancellation (on-account)	Yes	Standard

Customer Support

Req ID	Requirement Description	Covered in Odoo?	Odoo Fit
27	Chat widget & ticket logging to CRM	No	Integration
28	Auto SR creation (chat / call) & merge	No	Integration
29	SR reassignment & team views	Yes	Standard

Reporting & Analytics

Req ID	Requirement Description	Covered in Odoo?	Odoo Fit
30	Revenue tracking (monthly/yearly)	No	Integration
31	Revenue by vertical / parameters	No	Integration
32	Cost tracking & cost codes	No	Integration
33	P&L per account	No	Integration
34	SLA compliance reports	No	Integration
35	Support-transaction volumes	No	Integration
36	Backlog SRs exceeding SLA	No	Integration
37	Customer-satisfaction dashboard	Partial	Standard + Integration

Core Interfaces & Integration

Req ID	Requirement Description	Covered in Odoo?	Odoo Fit
I-1	Enterprise CRM workspace	Partial	Standard + Development
I-2	Vendor portal (registration, KPIs, payments)	No	Development
I-3	Customer self-service portal	Partial	Standard + Development
I-4	ERP/API integrations & scalability	No	Integration

Note:

“Covered in Odoo? = No” indicates that the capability is not available in Odoo out of the box and will need either custom development or an external integration to meet KUEC’s specification.

Odoo Standard Possible Utilization – Tailored to KUEC Center of Excellence (CoE)

In this section, we show how the core **Odoo 18 Enterprise** apps can be linked together, like stations on a single track to support KUEC’s end-to-end **Shared-Services Portal** life-cycle:

1. **Registration & Screening** (Website Forms → Portal → CRM)
2. **Service Catalogue & Ordering** (eCommerce / Sales → Subscriptions)
3. **Service Fulfilment** (Project / Helpdesk / Field Service)
4. **Vendor Collaboration & Procurement** (Purchase → Invoicing)
5. **Finance & Reporting** (Accounting → Spreadsheet → Power BI)
6. **Customer Support & Satisfaction** (Discuss → Survey)
7. **Governance & Compliance** (Documents, Approvals, Studio)

Rather than listing features in isolation, we kept each **BRD requirement** in view, mapped it to the closest out-of-the-box module, and described the hand-off that occurs when data moves from one module to the next. The objective is a practical playbook that shows where **configuration alone** delivers value, and where customization or external integration is unavoidable.

1 Registration & Screening

BRD Theme	Odoo Flow (Standard)	Key Built-in Features
Start-up / Vendor On-Boarding	Website > Form Builder captures registration data > auto-creates Partner record in Contacts > routes to CRM stage “Screening”.	CAPTCHA, attachment upload, GDPR consent, Server Action emails, Innovation & Procurement teams.
Approval Gate	Reviewer moves record to “ Approved ” stage; Approvals app logs decision & comments.	Multi-level approvals, activity scheduling, full audit trail.
Portal Activation	Portal invitation sent automatically; registrant sets self-password, sees personalized dashboard.	Single Sign-On (SAML/OAuth optional).
Auto-Notify	Automated Actions trigger system mails/chatter messages on stage change.	HTML templates per actor (Start-up, Investor, Vendor).

2 Service Catalogue & Ordering

BRD Theme	Odoo Flow (Standard)	Key Built-in Features
Catalogue Browsing	Website Shop / eCommerce lists “Service Packages” filters by Governmental vs Non-Governmental, Delivery Mode, and Eligibility.	Pricelists, attribute filters, -and multi-currency.
Eligibility Matrix	The portal user enters or already holds tags (“Subsidiary”, “Startup”). Website Builder shows only eligible items via the Domain filter.	Dynamic publish rules; no code needed.
Package Subscription / Retainer	“Subscribe” button converts to Sales → Subscription contract with billing cycle (monthly/annual).	Automatic invoicing, payment tokens, and renewal alerts.
Quote for Project-Based Service	RFP button opens Sales Quotation form; CoE Coordinator completes scoping; quote emailed to customer.	Sign on quote: online payment of deposit.

3 Service Fulfilment & Task Management

BRD Theme	Odoo Flow (Standard)	Key Built-in Features
Project-Based Services	Sales Order confirmation spawns a Project with tasks & milestones.	Gantt / Kanban views, project profitability.

Retainer / Ticketed Services	Subscription auto-creates a Helpdesk ticket each month, OR lets the customer raise an SR manually in the Portal.	SLA timers, timesheets, and billable hours.
22-Step Onboarding Package	Pre-configured Project Template (22 tasks) imported at startup profile approval.	Task checklist widget, progress bar.
Service Communication Thread	Every task/ticket has its own Discuss channel; vendor staff are added as followers from the Vendor Portal .	File sharing, emoji, @mentions.
Customer Satisfaction	On task/ticket closure, the Survey app auto-sends a 5-point CSAT form; scores feed Kanban 'Happy / Neutral / Unhappy'.	Conditional questions, dashboard.

4 Vendor Collaboration & Procurement

BRD Theme	Odoo Flow (Standard)	Key Built-in Features
Vendor Registration & Rating	Vendor record created, Purchase tags hold Service Categories; custom "Stars" field via Studio .	Vendor pricelists, scorecards.
Smart Routing	Python rule (custom) assigns incoming SR to preferred vendor; rule taps vendor category & star rating.	(Custom logic sits on top of Purchase / Project).
PO & 3-Way Match	CoE Coordinator approves vendor's proposal > auto-creates Purchase Order > Goods Receipt > Vendor Bill matched.	Duplicate-bill blocking, price variance warnings.

5 Finance, Wallets & Reporting

BRD Theme	Odoo Flow (Standard + BI)	Key Built-in Features
Billing & Refunds	Subscription invoices auto-post to Accounting ; credit-note wizard handles cancellations; payment acquirer refunds card (API).	Payment tokens, multi-currency, and Partial refunds.
On-Time Payer Wallet	Simple “Wallet” analytic account holds credit balance; applied on next invoice (custom but lightweight).	Analytic defaulting, negative invoice lines.
Revenue / Cost / P&L	Spreadsheet template pulls live data from Accounting, Purchase; publishes to Power BI via connector.	Pivot caching, scheduled exports.
SLA & Backlog KPIs	Helpdesk KPIs exposed via Odoo’s /JSON RPC; Power BI dataset refreshes nightly.	Native SLA statistics, tag filtering.

6 Customer Support & Live Chat

BRD Theme	Odoo Flow (Standard + Integration)	Key Built-in Features
Live Chat Widget	Odoo Live Chat embeds on portal pages; on the/helpdesk channel, join it creates a ticket automatically.	Chatbot hand-over, canned replies.
Call Logging	Odoo VOIP module logs inbound calls; missed call triggers a Helpdesk ticket.	Asterisk / SIP integration.

Ticket Merge	Built-in “Merge Tickets” wizard groups duplicates; SLA clock preserves the oldest timestamp.	Drag-drop merge, chatter history preserved.
---------------------	--	---

7 Governance, Documents & Approvals

BRD Theme	Odoo Flow (Standard)	Key Built-in Features
Service Cards & Version Control	Each service has a Product Template; CoE Admin edits via Studio ; revisions are tracked in Documents .	Check-in/out, versioning.
Digital Approvals	Approvals app routes POs, price exceptions, vendor onboarding forms; fully timestamped.	PDF attachments, resubmit loop.
Policy & License Repository	All master data (licenses, policies) are stored in Documents with expiry alerts 60 days prior.	Access groups, tag search.

Why It Matters for KUEC

- **Faster Go-Live** – 80 % of the CoE requirements align with native Odoo workflows; configuration delivers value before custom code starts.
- **Single Source of Truth** – Contacts, SRs, projects, invoices, and surveys all share the same database, cutting manual reconciliations.
- **Scalable Roadmap** – Future AI routing, vendor chatbots, or advanced BI dashboards can plug into the same API layer with minimal refactoring.


Whenever a BRD line item genuinely **exceeds standard capability**, we have flagged it in the Compliance Matrix as **Development** or **Integration**; otherwise, the tables above demonstrate how **Odoo Standard** can be deployed immediately to cover core CoE processes.

Data-Migration & Cleansing Plan

We will migrate all legacy customer, vendor, and service-catalogue data into Odoo in a three-wave approach:

Wave	Source Systems	Target Models	Cleansing & Validation Steps	Owner
1	Excel master lists (Start-ups, Subsidiaries, Vendors)	(Contacts) incl. tags for Eligibility & Customer Class	- Remove duplicates - ISO address / phone format - Emirate & license-number regex checks	KUEC Data + Kaizen
2	Current SR tickets (SharePoint / Mailbox)	helpdesk.ticket + attachments	- Map old categories to new Service Codes - Auto-assign historic SLA outcomes	Kaizen
3	Historical invoices & vendor bills (ERP)	account.move	- Balance control accounts - Tie to analytic tags for cost center P&L	KUEC Finance

Integration Architecture

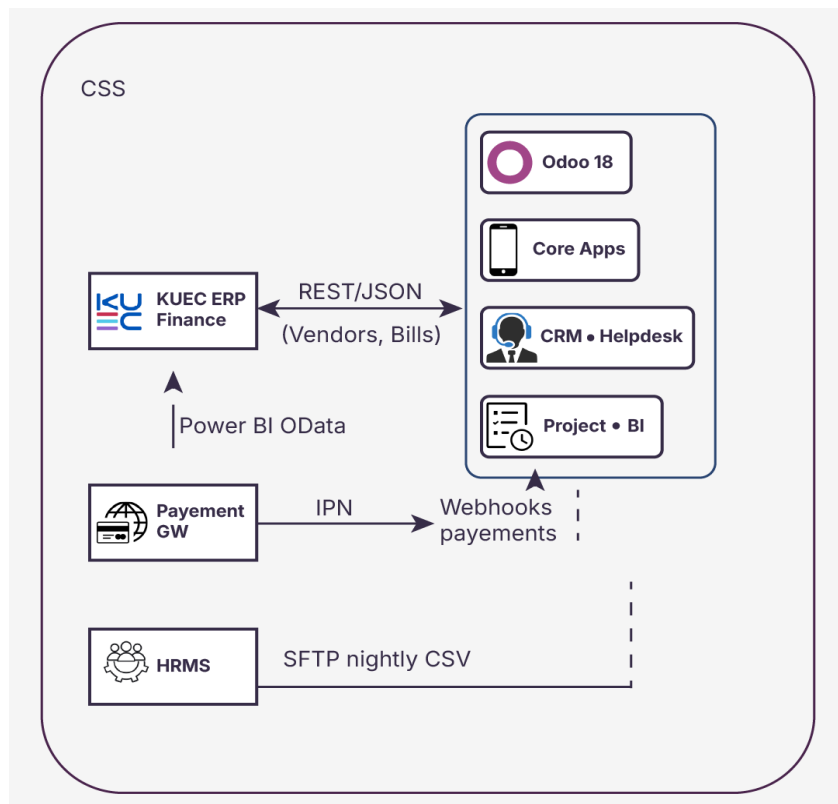

Training Approach: “Explain → Show → Do → Coach”

Kaizen Principles will deliver a structured training program to ensure all KUEC user groups—internal teams, vendors, and customers—are confident and self-sufficient in using the new portal and back-office system. Our approach is based on the

“Explain → Show → Do → Coach” model, which maximizes both knowledge retention and real-world application.

Phase 1: Explain

We begin each training module by clearly **explaining** the why and what behind the system feature or process.

- **10–15 minute** briefing sessions aligned to real KUEC use cases (e.g., registering a startup, routing a service request).
- Delivered live or pre-recorded via Google Meet.
- Materials: PDF Quick Reference Guides, Arabic & English.

Phase 2: Show

Next, we **demonstrate** the feature live in the system, using Demo data and the actual KUEC configuration.

- Step-by-step walkthroughs in Odoo (e.g., confirming a purchase order, responding to a vendor quote).
- Recorded screen shares added to KUEC’s internal training library.
- Split by role: CoE Coordinator, MIS Analyst, Vendor, Customer.

Phase 3: Do

Users then **practice** the process themselves inside the UAT (test) environment.

- “Role-play” exercises: simulate SR routing, service delivery milestones, vendor invoice processing.
- Users follow the process with guidance materials but without intervention.
- Hands-on tasks are tracked via checklists to monitor progress and identify knowledge gaps.

Phase 4: Coach

Finally, our trainers **observe** and provide 1:1 or small-group coaching sessions to reinforce learning.

- Shadowing during the pilot phase (e.g., watch the first vendor onboarding or ticket resolution).
- Corrections and tips offered live, with a follow-up summary sent to each participant.
- This phase continues into Week 1 of go-live as part of the Hypercare plan.

Training Schedule Snapshot:

Audience	Training Format	Language	Duration	Materials
CoE Coordinators	Live + recorded	EN/AR	3 x 1.5h	Role manual, videos
Vendors	Video + sandbox tasks	EN/AR	Self-paced	Portal guide, checklist
Internal Departments	Live session + follow-up	EN/AR	1 x 2h	Process map, SOP
Startups / Customers	Walkthrough videos in the portal	AR preferred	< 10 min each	FAQ, in-app video

This model ensures **each user learns not just where to click, but when, why, and what to do next**, reinforcing KUEC's vision of a modern, intuitive, and service-focused digital experience.

Assumptions & Exclusions

#	Assumption / Exclusion	Impact if False
A1	Legacy data provided in agreed format before Sprint 1	Timeline slip $\approx$ 1 week
A2	Payment gateway onboarding starts in Week 1	Delay in go-live payments
E1	Arabic translations for UI provided by KUEC	Minor delay in UI delivery

SLA & Support Model

Tier	Example	Response	Resolution	Escalation
L1	Password reset	1 h	4 h	–
L2	Minor bug	4 h	1 bd	L3 after 8 h
L3	Outage	30 min	4 h	CTO

Project Implementation Plan & Timeline

This section outlines our proposed **compressed implementation roadmap**, designed to deliver the entire KUEC CoE Shared Services Portal in **under 2 calendar months**.

Rather than spreading delivery across traditional agile sprints, we have structured the work into **four functional implementation tracks**, each with focused teams working in parallel to accelerate time to value.

The schedule is anchored to a **2 September 2025** kickoff. All milestones are subject to adjustment based on KUEC resource availability, data readiness, or integration partner alignment.

On-Site Discovery First

The project begins with a **5-day on-site Discovery & Alignment workshop** during the first week of September. This workshop is attended by key stakeholders across CoE Coordination, MIS, Procurement, and Finance.

Objectives include:

- Finalizing scope and ownership per the BRD requirement
- Validating data structure, user stories, and business rules
- Confirming acceptance criteria and reporting expectations

This ensures that the upcoming configuration and development work is **rooted in real user context**, reducing risk and rework.

Functional Delivery Tracks

Track	Duration	Key Deliverables
Track 1: Registration & Interfaces	1 week	Startup/vendor registration flows, approval engine, portal activation, role-based views (Customer, Vendor, CoE Coordinator)
Track 2: Catalogue & Logic	2 weeks	Service catalogue (gov + non-gov), subscription model, pricing rules, eligibility filters, smart routing logic

Track 3: Fulfilment & Support	1 week	Onboarding packages, project-based and retainer fulfilment journeys, helpdesk workflows, and customer satisfaction surveys
Track 4: Finance & Reporting	2 weeks	Wallet & refund engine, invoice logic, integration touchpoints (ERP & payment), Power BI datasets (SLA, revenue, CSAT)

Key Milestones & Timeline

Date	Milestone
1st Week	Project Kickoff & Discovery Workshop
2nd week	Registration Module
4th week	Catalogue Logic Fully Configured
6th week	Fulfilment & Support Demo Sign-Off
6th week	Finance Logic Ready for Validation
7th week	Full System Go-Live
8th – 12th week	Hypercare, knowledge transfer, and Go-Live extension to all users

Execution Principles

1. **Parallel teams** are assigned per track to maximize velocity
2. **Shared project board** (Odoo Project) visible to KUEC and Kaizen team for daily tracking
3. Weekly RAID log reviews with KUEC leadership
4. All major releases are tested and staged on UAT before go-live
5. Arabic and English UI/UX validated in each module

Appendix C — Proposed UI Mockups (Odoo 18 EE Theme)

The following visuals present conceptual user interface mockups of the **KUEC Center of Excellence Self-Service Portal**, designed in the official **Odoo 18 Enterprise** style.

They illustrate the complete workflow from portal entry to service request fulfilment, support, and administrative configuration.

Each mockup directly maps to functional requirements in the BRD and Service Catalogue, making it easier for all stakeholders to visualise how the proposed solution will look and operate.

Figure 01 — Portal Landing Dashboard

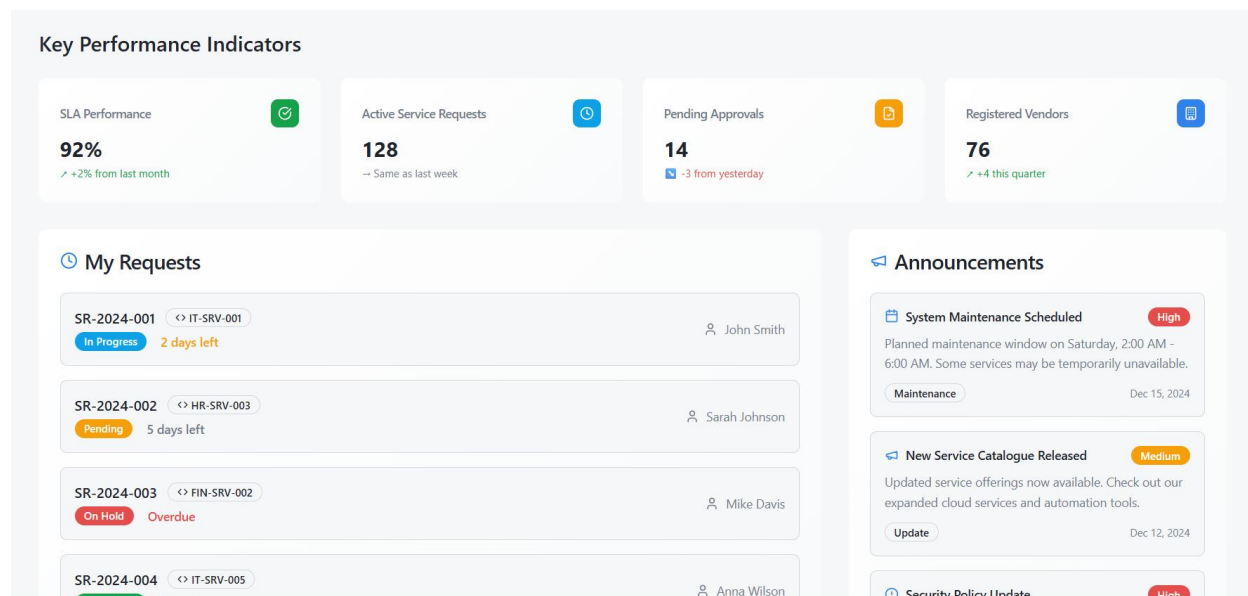


Figure 02 — Customer Registration (Start-Up)

Purpose: Allows new startup customers to register, upload compliance documents, and submit for eligibility screening. Progress bar shows completion (Company Profile → Documents).

Registration Progress
Step 1 of 3

Company Profile33%

1Company Profile
Basic company information

2Documents
Upload compliance documents

3Review & Submit
Final review and eligibility screening

Company Profile
Basic company information

Company Name *
Business Type *

Industry *
Website

Contact Email *
Contact Phone *

Emirate
Founded Year

Figure 03 — Service Catalogue (Governmental & Non-Governmental)

Purpose: Let customers browse available services with filters for type, delivery mode, and eligibility. Each service card shows Service Code, title, and pricing, with a link to full details.

Filters

Clear all

Search Services

Q Search by title or code...

Category

All categories

Delivery Model

All delivery models

Eligibility

☐ Startup
 ☐ Subsidiary
 ☐ Internal

6 services found

Most Popular

GOV-EST-SUB-BNDL-PRO

GOV

Business License & Establishment

Complete business setup package including trade license, visa processing, and bank account opening

Delivery: Project

Duration: 4-6 weeks

Eligibility: Startup Subsidiary

\$ AED 15,000

View Details

NON-MKT-DIG-RET-ALL

PRIV

Digital Marketing Suite

Comprehensive digital marketing services including SEO, social media, and content marketing

Delivery: Retainer

Duration: Ongoing

Eligibility: Startup Subsidiary Internal

\$ AED 8,500/month

View Details

GOV-VIS-EHP-BNDL-PRO

GOV

Employee Visa Processing

Complete visa processing for new employees including medical, Emirates ID, and labor card

Delivery: Project

Duration: 2-3 weeks

Eligibility: Startup Subsidiary Internal

\$ AED 3,200

View Details

NON-HR-REC-RET-SUB

PRIV

Recruitment & Talent Acquisition

Professional recruitment services for technical and managerial positions

Delivery: Retainer

Duration: 3-6 months

Eligibility: Subsidiary Internal

\$ AED 12,000/month

View Details

Figure 04 — Create Service Request

Purpose: Form to submit a new request. Supports Project-Based (scope, target date, budget) or Retainer (billing cycle, start date, wallet credit) modes.

Service Request Details

Choose your service delivery model and provide request details

 Project-Based

 Retainer

Service Category

Select service category

Priority

Select priority

Project Scope

Describe the scope of work, deliverables, and requirements...

Provide a detailed description of what you need (minimum 10 characters)

Target Completion Date

Pick a date

Budget (AED)

\$ e.g., 50,000

Enter your estimated budget in AED

Additional Notes (Optional)

Any additional information or special requirements...

Figure 05 — Vendor Payments & CSAT

Purpose: Vendor view to track scheduled/paid payments linked to service milestones and review customer satisfaction scores by service.

Vendor Portal — Payments & Ratings

Track your payments and customer satisfaction ratings


Next Payment: AED 12,500
 Due 12/09/2024 • IT Infrastructure Setup

Total Pending
AED 36,250


Total Earnings
AED 57,500
Paid to date


Average Rating
4.6 ★★★★★
Based on 78 reviews


Active Projects
4
In progress

Scheduled Payments

Paid

CSAT

Scheduled Payments
Upcoming and pending payments for your projects

Project/SR	Amount	Status	Due Date	Milestone	Actions
SR-2024-0156 IT Infrastructure Setup	AED 12,500	 Scheduled	 9/12/2024	Phase 2 Completion	
SR-2024-0189 Digital Marketing Campaign Q3	AED 8,750	 Scheduled	 9/20/2024	Campaign Launch	
SR-2024-0201 HR System Implementation	AED 15,000	 Processing	 9/15/2024	Final Delivery	
SR-2024-0143 Legal Compliance Review	AED 5,500	 Overdue	 8/30/2024	Report Submission	

Figure 06 — Dispute Resolution Case

Purpose: Central case view for disputes between customer and vendor. Shows threaded communications, linked SR, reason, SLA target, and escalation actions.

Dispute Case DC-002

Manage and resolve service delivery disputes

Case Information

High Under Investigation

Linked SR	Reason	SLA Target	Created
SR-2024-0156	Service delivery delay and quality issues	72 hours	3/15/2024

SLA Progress 65% of time elapsed

Conversation Thread

Three-party communication between customer, vendor, and CoE coordinator

Ahmed Al-Mansouri Emirates Trading LLC 3/15/2024, 2:30:00 PM

I am raising a formal dispute regarding the service delivery for SR-2024-0156. The project was supposed to be completed by March 10th, but we are still waiting for the final deliverables. Additionally, the quality of work delivered so far does not meet the agreed specifications.

Attachments:

original_requirements.pdf	2.4 MB	Download
project_timeline.xlsx	1.1 MB	Download

Fatima Al-Qasimi KUEC CoE Team 3/15/2024, 3:15:00 PM

Thank you for raising this dispute, Ahmed. I have initiated a formal investigation into this matter. I will be coordinating between all parties to resolve this issue within our SLA.

Type your message here...

Attach File

Send Message

Escalation

If this dispute cannot be resolved at the current level, escalate to L2 management for further review.

Escalate to L2

Participants

Ahmed Al-Mansouri
Emirates Trading LLC
Customer

Sarah Connor
Digital Solutions LLC
Vendor

Fatima Al-Qasimi
KUEC CoE Team
Coordinator

Figure 07 — Project-Based Fulfilment Orchestration

Purpose: Visualises the workflow of project-based services. Kanban columns (To Do, In Progress, Review, Done) show task stages; right mini-Gantt shows timelines.

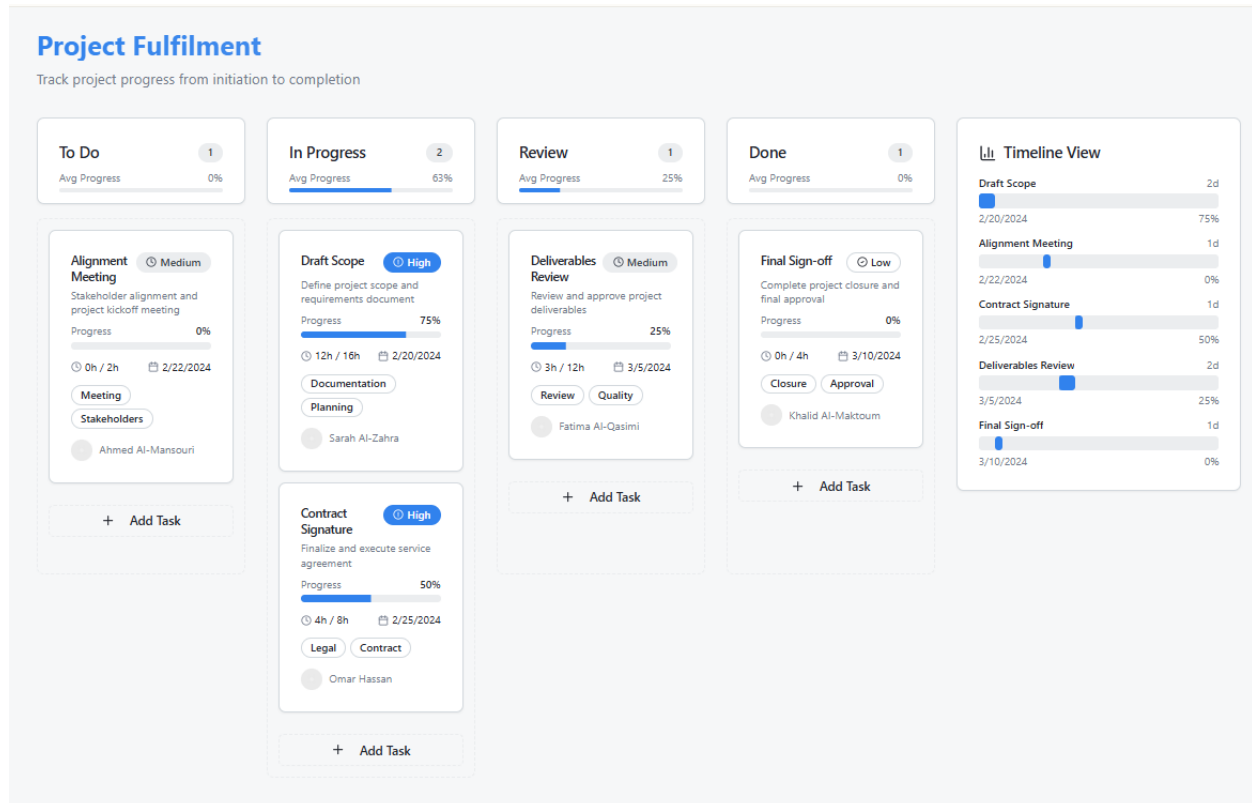


Figure 08 — Retainer Fulfilment Orchestration

Purpose: Displays recurring service tickets grouped by month. SLA compliance shown with green/amber status pills; includes vendor assignment and CSAT scores.



Retainer Fulfilment

Track and manage ongoing retainer service deliveries and SLA compliance

Filters & Search

Search

Search tickets, services...

Status

All Statuses

SLA Status

All SLA Status

Clear Filters

July 2024

3 tickets • 2 resolved • 0 SLA breached

Avg CSAT
★ 4.7

Resolution Rate
67%

Ticket #	Service	Subscription	SLA	Status	Vendor	CSAT
RET-2024-001	Digital Marketing Created: 7/5/2024	Marketing Pro	On Track 18h / 24h	Resolved	Marketing Experts	★ 4.8
RET-2024-002	IT Support Created: 7/12/2024	IT Essential	At Risk 20h / 24h	In Progress	Digital Solutions LLC	Pending
RET-2024-003	HR Consulting Created: 7/20/2024	HR Premium	On Track 8h / 48h	Closed	HR Partners	★ 4.6

August 2024

3 tickets • 2 resolved • 1 SLA breached

Avg CSAT
★ 4.1

Resolution Rate
67%

Ticket #	Service	Subscription	SLA	Status	Vendor	CSAT
RET-2024-004	Legal Advisory Created: 8/3/2024	Legal Standard	Breached 75h / 72h	Resolved	Legal Advisory Group	★ 3.2
RET-2024-005	Financial Planning Created: 8/15/2024	Finance Pro	On Track 24h / 48h	Closed	Finance Pro Services	★ 4.9

Support

Get help with your services and manage support tickets

Live Chat Support

Chat with our support team in real-time

LA Support Agent 6:30:00 PM

Hello! Welcome to KUJEC CoE Support. My name is Layla and I'm here to help you today. How can I assist you?

You 6:31:00 PM

Hi Layla, I'm having issues with my service request SR-2024-0156. The vendor hasn't provided any updates for the past week and I'm concerned about the timeline.

LA Support Agent 6:32:00 PM

I understand your concern. Let me look up the details for SR-2024-0156. Can you please confirm the service category for this request?

You 6:33:00 PM

Type your message here...

Agent online

Send

My Tickets

View and manage your support tickets

Merge (0)

#	Subject	Channel	SLA	Owner	Status
TKT-2024-001	Service request delay - SR-2024-0156 3/18/2024	Chat	On Track 1h 25m	LA Layla Al-Mansoori	In Progress
TKT-2024-002	Invoice discrepancy for February services 3/17/2024	Web	At Risk 45m	AH Ahmed Hassan	Waiting for Customer
TKT-2024-003	Access issues with vendor portal 3/16/2024	Call	Breached Overdue by 2h	SA Sarah Al-Zahra	Open
TKT-2024-004	Request for new vendor onboarding 3/15/2024	Web	On Track 2d 5h	OA Omar Al-Rashid	In Progress
TKT-2024-005	Quality concerns with recent deliverables 3/14/2024	Chat	On Track 4h 30m	FA Fatima Al-Qasimi	Resolved

5 tickets total 3 active tickets

Figure 9 — Customer Support (Chat & Ticket Tracking)

Purpose: Integrated customer support view. Live chat transcript on left; ticket list on right with ability to merge duplicates.

Conclusion

The proposed **KUEC Partner Self-Service Catalog Portal** has been meticulously mapped and visualized based on the **BRD** and **Service Catalog** requirements. With the use of **Odoo 18 EE** as the foundation, the solution delivers an intuitive, fully integrated, and scalable platform capable of supporting all KUEC operations—from registration and vendor collaboration to invoicing and reporting. Each core requirement has been addressed through Odoo's **out-of-the-box** capabilities, with additional customization and integration planned where necessary to meet specific needs.

Key Points:

1. **Optimized Solution:** The solution leverages Odoo's full capabilities, ensuring minimal development time while maximizing functional benefits, particularly in the areas of registration, customer service, and financial management.
2. **Realistic Visualizations:** High-fidelity mockups allow KUEC stakeholders to easily visualize the end-user experience and the impact on their operations.
3. **Scalable Roadmap:** Future-proof integrations (e.g., AI routing, Power BI analytics) are seamlessly aligned to Odoo's extensible framework, providing a growth path for the portal.
4. **Training and Support:** The training approach ensures that KUEC's teams—ranging from vendors to internal departments—are equipped with the skills and knowledge to operate the portal efficiently from day one.

In summary, this proposal outlines how Kaizen Principles will work collaboratively with KUEC to implement a robust, efficient, and future-oriented self-service portal, leveraging **Odoo 18 EE** and enhancing it with necessary customizations. This will not only fulfill immediate operational requirements but will also lay the foundation for sustained growth, efficiency, and innovation within KUEC's shared service model.
